



PROJECT INSPECTION

Generated by Safety Compliance App www.safetycompliance.com | www.safetycomplianceapp.com

Company	Bay City Boiler	Type of Inspection:	BC Safety Inspection
Project	GC Farms Hollister	Date of Inspection	January 27, 2025
Inspector Name	Tomas Lopez	Time of Inspection	10:03 AM

NOTES

16
Items Inspected

8
Satisfactory

1
Unsatisfactory

7
N/A

Work being conducted is firing head replacement.

INSPECTION ITEMS

General

Is emergency equipment available, including first aid kit(s) and fire extinguisher(s)? **Satisfactory**

Is safety documentation available (Written Safety Programs, SDS, Tailgate Meetings) **Satisfactory**

Is drinking water and shade set up sufficient for the amount of workers? **Satisfactory**

Is Personal Protective Equipment being worn as required?: Eye, ear, glove, respirator, shoes, and face shield? **Satisfactory**

Are scaffolding safety procedures being followed and inspected?: Fully planked, guardrails in place, toe boards, and ladders? **N/A**

Are hand and power tools being used safely? Are guards installed on tools? **Satisfactory**

Is good housekeeping being maintained?: Clean work area and sufficient lighting in work area? **Satisfactory**

Is fall protection in place where required? Fall harness and lanyard inspected?

N/A

Are ladders being used safely? Was the ladder inspected and in good condition?


N/A

Are confined space safety procedures being followed?: Permit posted? Was the customer informed of the operation?

Satisfactory

Comment

Documentation

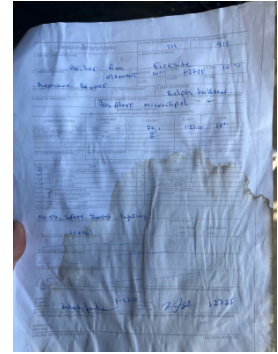

Hot work permit posted? Is the welding screen utilized and fire watch established?

N/A

Are scissor lifts / elevated platforms being used safely?

N/A

Are boom lifts and other aerial devices being used safely?

N/A

Are electrical items being used safely?

N/A

Are all other tasks being performed safely?


Satisfactory

Is lockout/tagout included in the operation? Are proper procedures being followed?

Unsatisfactory

Comment

Corrective action

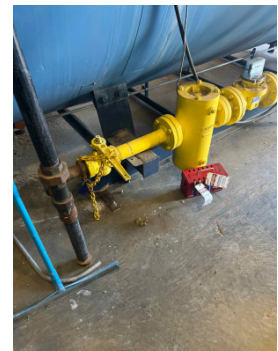

Electrical and gas were isolated but no chains on gas valve nor lock box

-
